



# Access Compliance Report Public Rights-of-Way (Curb Ramps)




Main Street: O\_NEILL\_DR Cross Street: BENJAMIN\_DR Location: NW

ADA ID: RPRK211020170451 Ramp Type: Type 1 - Perpendicular Initial Pass/Fail: Pass Overall Compliance: No Severity Score: 25

## Codes/Mitigation Info/Possible Solution

## Field Measurements/Component Compliance

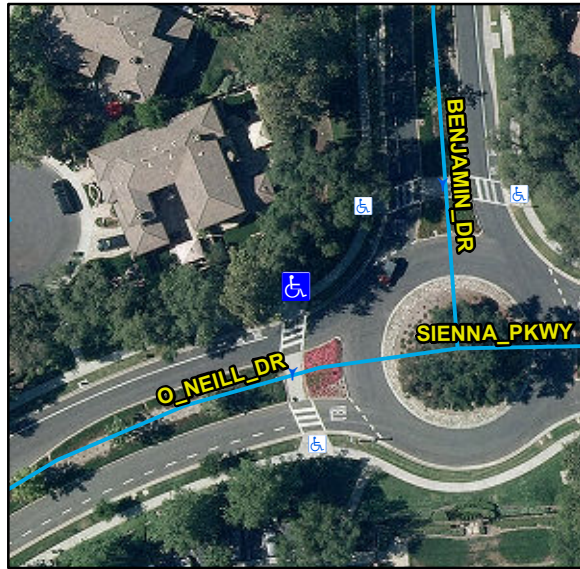

### Possible Solutions:

Remove & Replace Entire Ramp. Remove & Replace Gutter.

### Surveyor Notes:

N/A

### OC Std/PROW:

R304.2.2, R304.2.1, R304.2.2-Perp, R304.3.2-Para, R304.5.3, R305, R304.5.4, STD 1115

Total Cost: \$ 3332

Parcel ID Number 759-201-82  
Ramp Island Or Median None  
Ramp Orientation NonDiag  
Google Street View Link:

[http://www.google.com/maps/@?api=1&map\\_action=pano&viewpoint=33.57079505,-117.63890444](http://www.google.com/maps/@?api=1&map_action=pano&viewpoint=33.57079505,-117.63890444)

Street 1 Name O\_NEILL\_DR  
Stop Condition-Street 1 YieldSign  
Street 2 Name BENJAMIN\_DR  
Stop Condition-Street 2 N/A

## Obstruction and Utility Measurement/Component Compliance

| Compliance | Description            | Data | Compliance | Description        | Data |
|------------|------------------------|------|------------|--------------------|------|
| Yes        | Obstructions Present?  | No   | N/A        | Utilities Present? | No   |
|            | Obstruction Types      | N/A  |            | Utility Types      |      |
|            | Obstruction Dimensions | N/A  |            |                    | N/A  |

| Compliance | Description                           | Data | Compliance | Description                   | Data   |
|------------|---------------------------------------|------|------------|-------------------------------|--------|
| N/A        | Ramp Length (in)                      | 126  | N/A        | Flare Type LT                 |        |
| Yes        | Ramp Width (in)                       | 48   |            |                               | Sloped |
| Yes        | Ramp Run Slope (%)                    | 6    | Yes        | Flare Slope LT (%)            | 7.9    |
| Yes        | Ramp Cross Slope (%)                  | 0.8  | N/A        | Flare Traversable LT          | Yes    |
| N/A        | Landing Present                       | No   | N/A        | Flare Type RT                 |        |
| N/A        | Landing Length (in)                   | N/A  |            |                               | Sloped |
| No         | Landing Width (in)                    | N/A  | Yes        | Flare Slope RT (%)            | 6.4    |
| No         | Landing Run Slope (%)                 | N/A  | N/A        | Flare Traversable RT          | Yes    |
| No         | Landing Cross Slope (%)               | N/A  | No         | DWS Provided                  | No     |
| N/A        | Landing Movement Obstructed?          | Yes  | N/A        | DWS Contrast                  | N/A    |
|            | Landing Movement Type                 | Curb | N/A        | DWS Length (in)               | N/A    |
| N/A        | Landing Shared                        | N/A  | N/A        | DWS Full Width                | N/A    |
| N/A        | Clear Space                           | N/A  | N/A        | DWS Offset Left (in)          | N/A    |
| N/A        | Clear Space To Crosswalk (in)         | N/A  | N/A        | DWS Offset Right (in)         | N/A    |
| N/A        | Marked Crosswalk 1                    | Yes  | N/A        | Marked Crosswalk 2            | N/A    |
|            | Crossing 1 Direction                  | S    |            | Crossing 2 Direction          | N/A    |
|            | Marked Crosswalk 1 Width (in)         | 144  |            | Marked Crosswalk 2 Width (in) | N/A    |
| Yes        | Ramp Inside Crosswalk 1               | Yes  | Yes        | Ramp Inside Crosswalk 2       | N/A    |
|            | Crossing 1 Slope (%)                  | 1    |            | Crossing 2 Slope (%)          | N/A    |
|            | Crossing 1 Cross Slope (%)            | 2.5  |            | Crossing 2 Cross Slope (%)    | N/A    |
| Yes        | Gutter Ponding                        | No   | No         | Curb Slope                    | 7.5    |
| Yes        | Gutter Lip Height (in)                | 0    |            | Road Run Slope (%)            | N/A    |
| No         | Gutter Run Slope (%)                  | 9.1  |            | Road Cross Slope (%)          | N/A    |
| Yes        | Gutter Cross Slope (%)                | 0.7  |            |                               |        |
| Yes        | Overall Surface Condition: Acceptable |      | Yes        | Perp Joint Present            | Yes    |
|            | Cross Gutter Present?                 | No   |            | Spandrel Present?             | No     |
|            | Replace Cross Gutter?                 | N/A  |            | Replace Spandrel?             | N/A    |

