REINFORCEMENT BENDING SCHEDULE

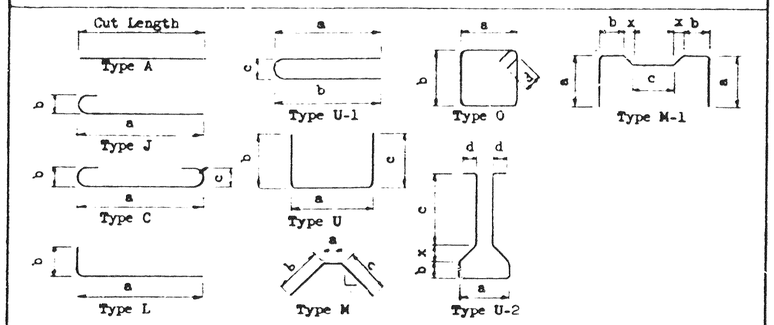

ALL DIMENSIONS ARE OUT TO OUT OF BARS

MARK NO.	QUAN.	TYPE	BAR SIZE	DIMENSIONS a	b	c	d	x	CUT LENGTH	LOCATION OR REMARKS
601	608	U	#6	3'-9"	1'-3"	1'-3"			6'-3"	A
702	32	A	#7						38'-0"	
603	64	U	#6	1'-6	3'-0"	3'-0"			7'-6"	
604	16	U	#6	4'-0"	1'-3"	1'-3"			6'-6"	
705	14	A	#7						2'-8"	
806	16	A	1"φ						2'-0"	

ISSUED FOR CONSTRUCTION

NOTES:
1. All re-bars shall be tagged with contract no. followed by dash and Pc. Mk. No.
   Example:
2. A L 9

JOB SECOND STR. BRIDGE OVER ALISO CREEK FOR ORANGE COUNTY HWY. DEPARTMENT	ROCKWIN PRESTRESSED CONCRETE CORP. 13440 E. IMPERIAL HIGHWAY SANTA FE SPRINGS, CALIFORNIA	R.B.S #1
JOB NO. 6058 DATE 6-29-60 BY Z.M.		SHT 1 OF 1
